

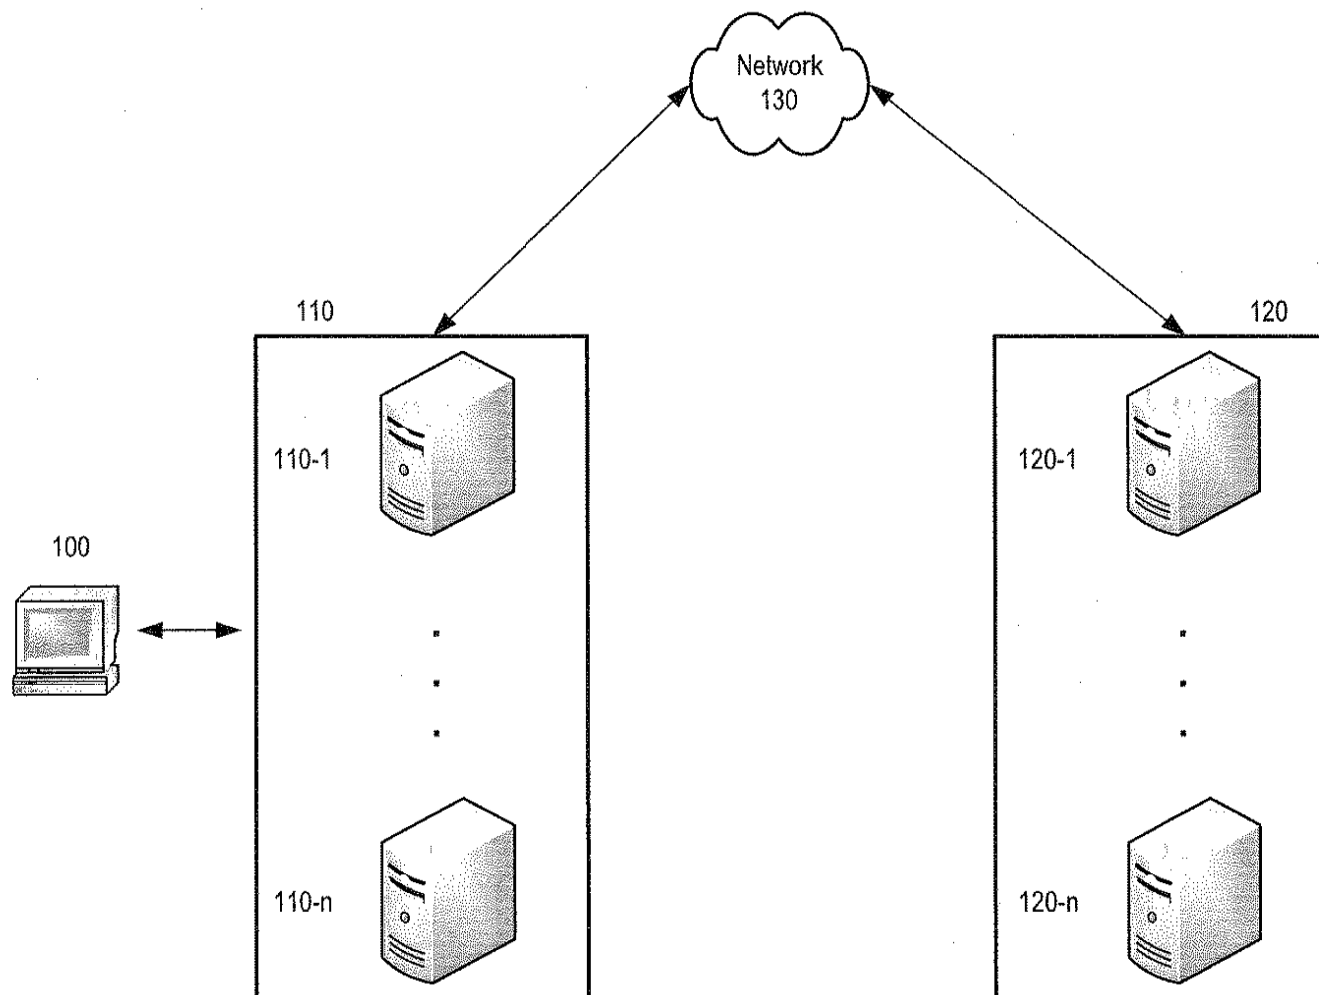


FIG. 1

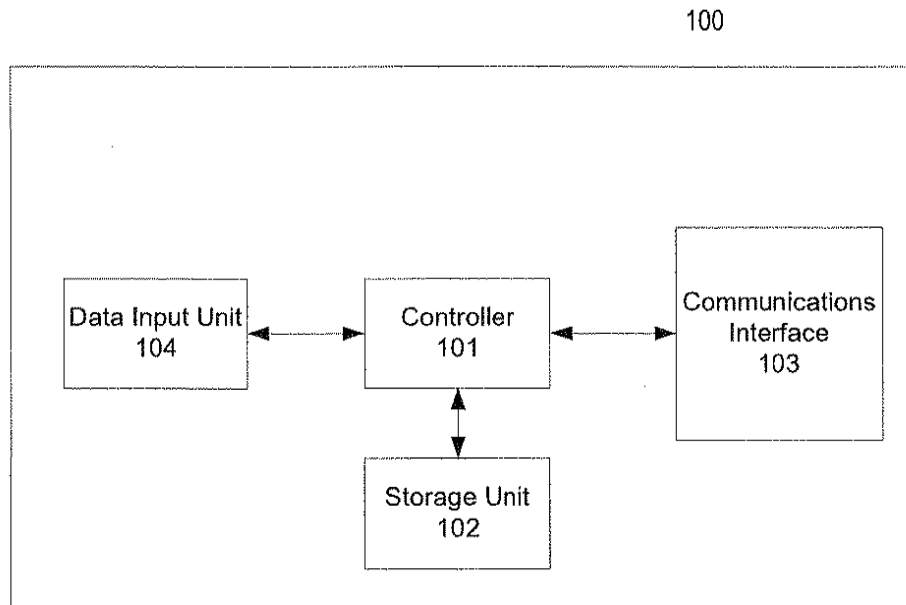


FIG. 2

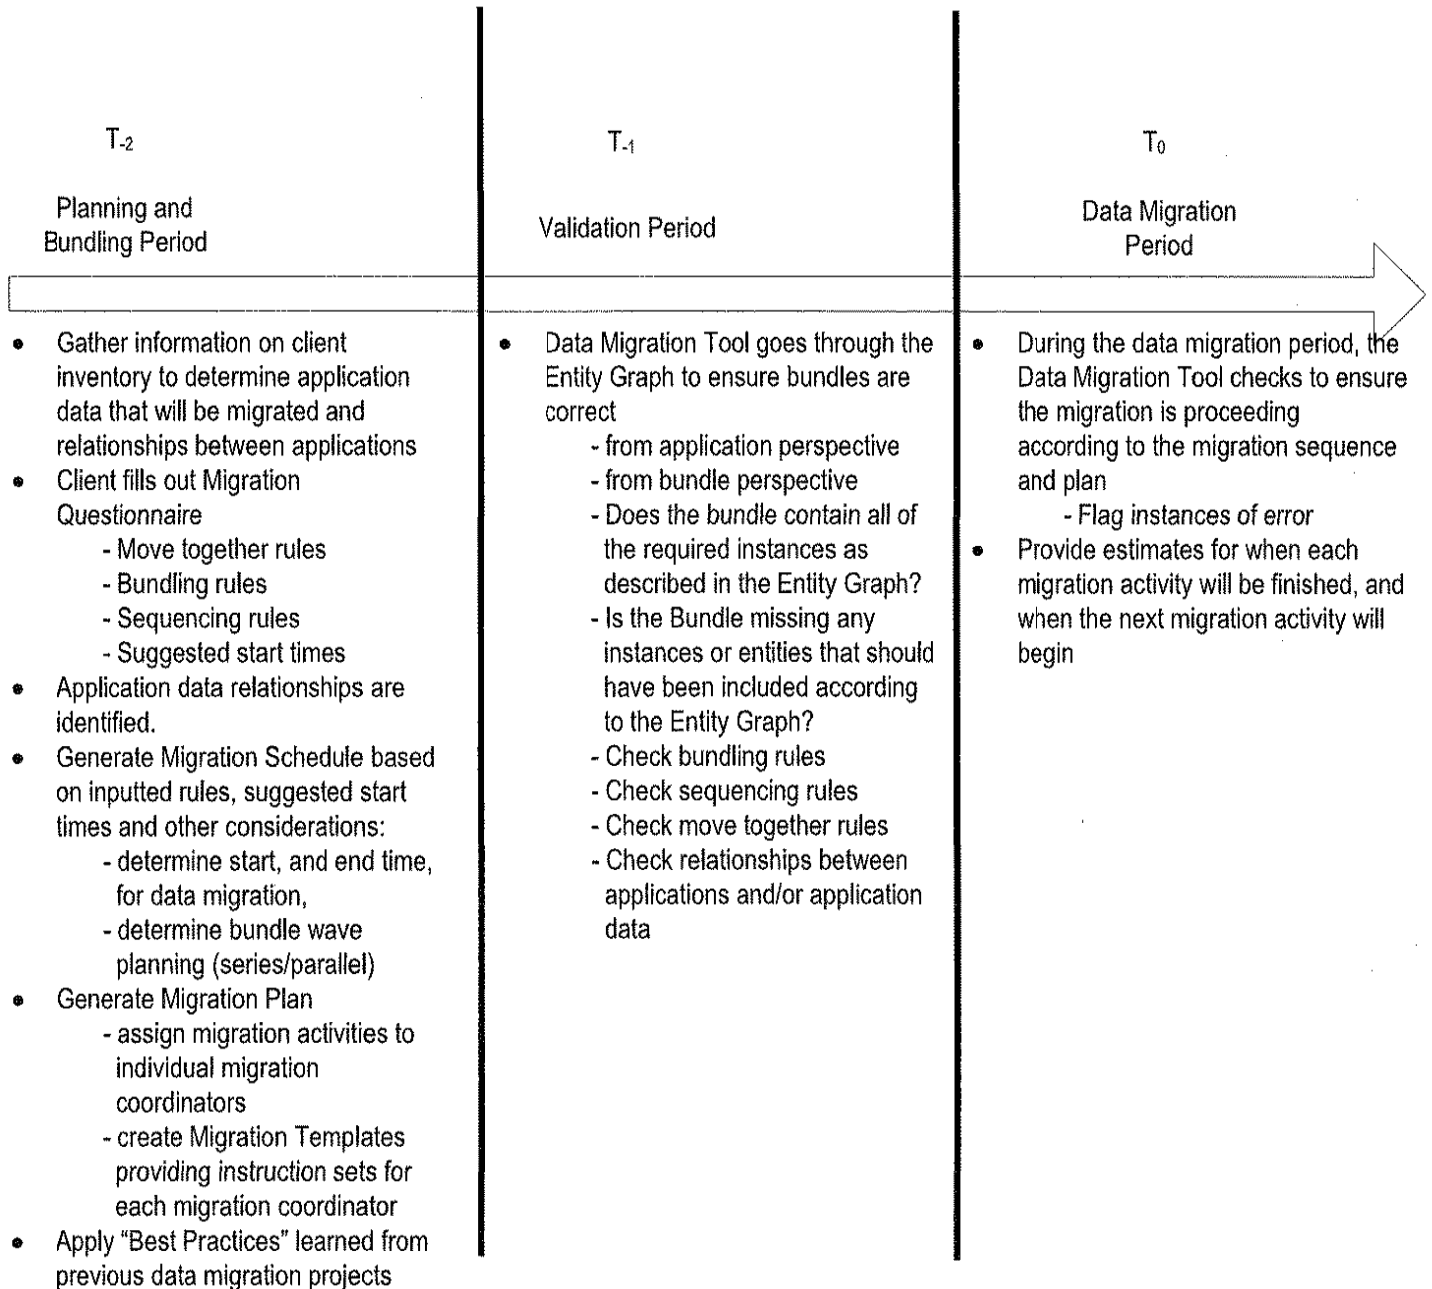


FIG. 3


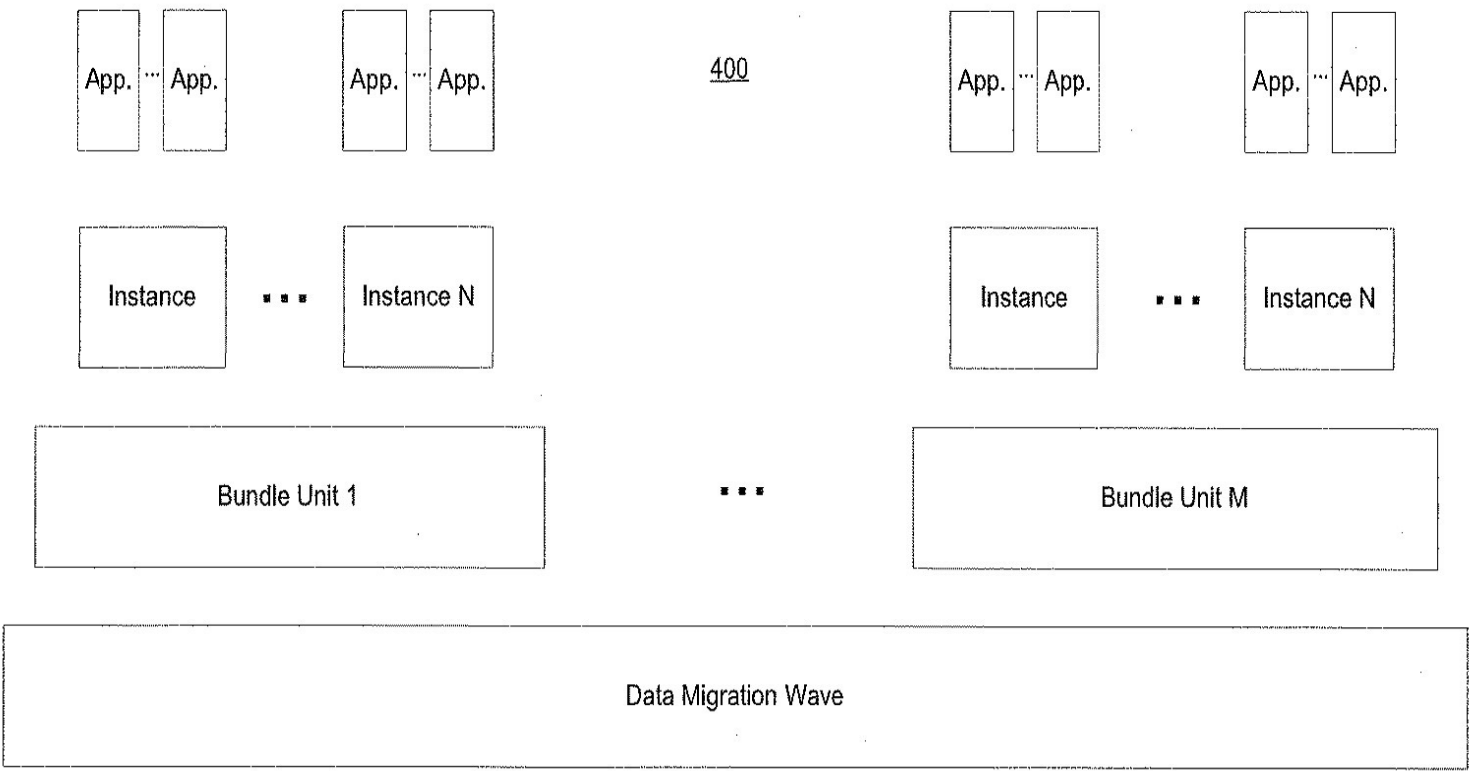



FIG. 4

500-A



Application runs on instance

Instances must move together



500-B

Resulting Bundles:




FIG. 5

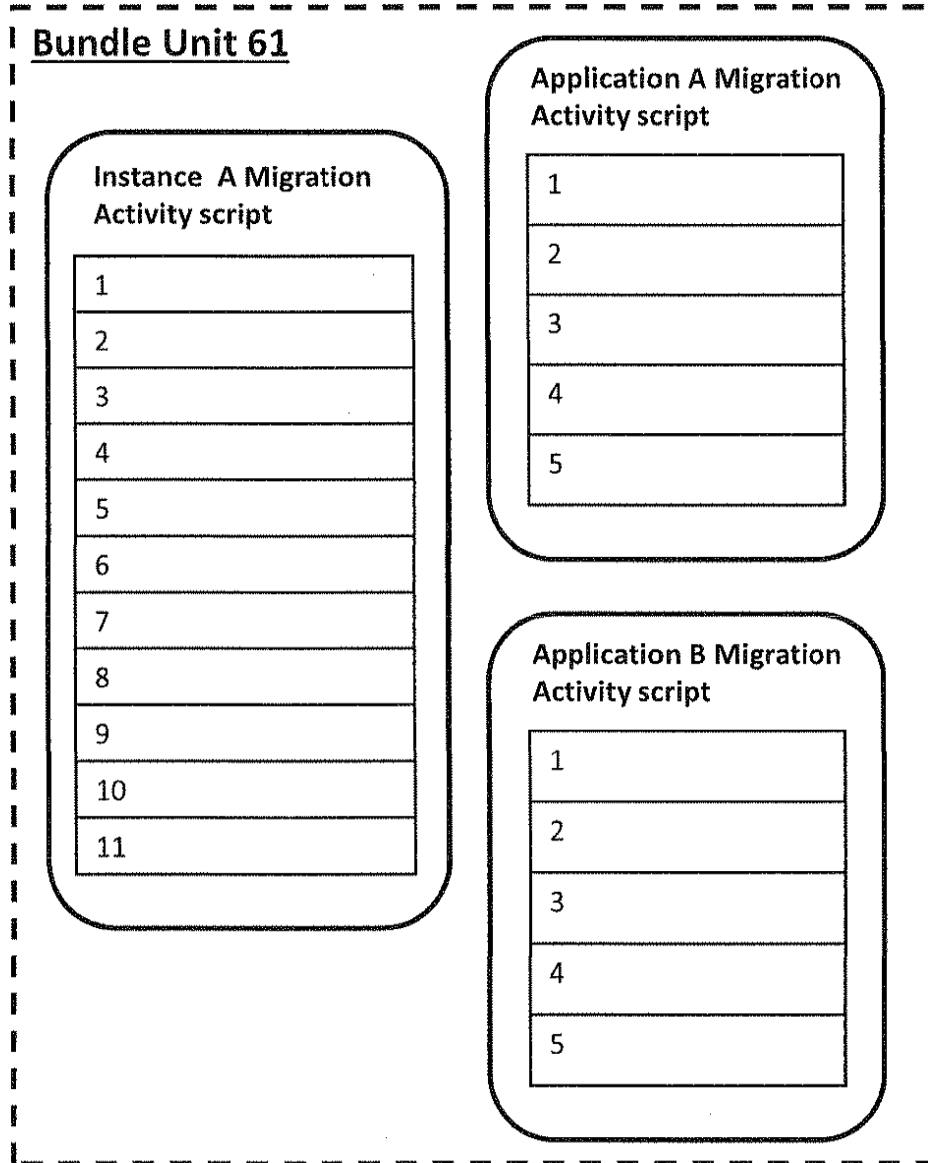


FIG. 6A

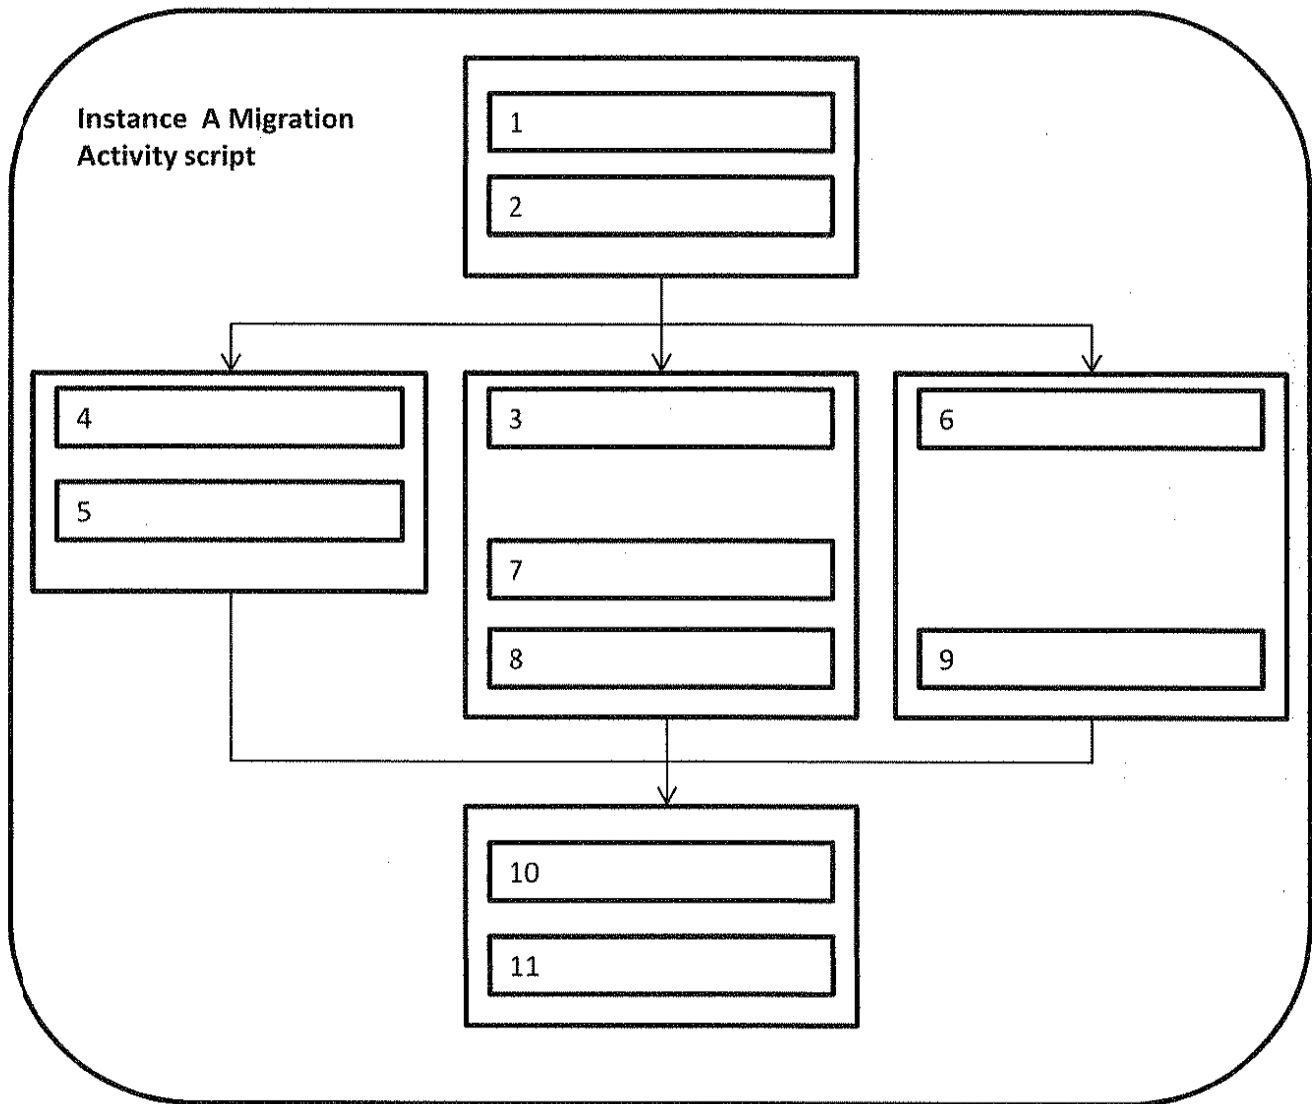


FIG. 6B

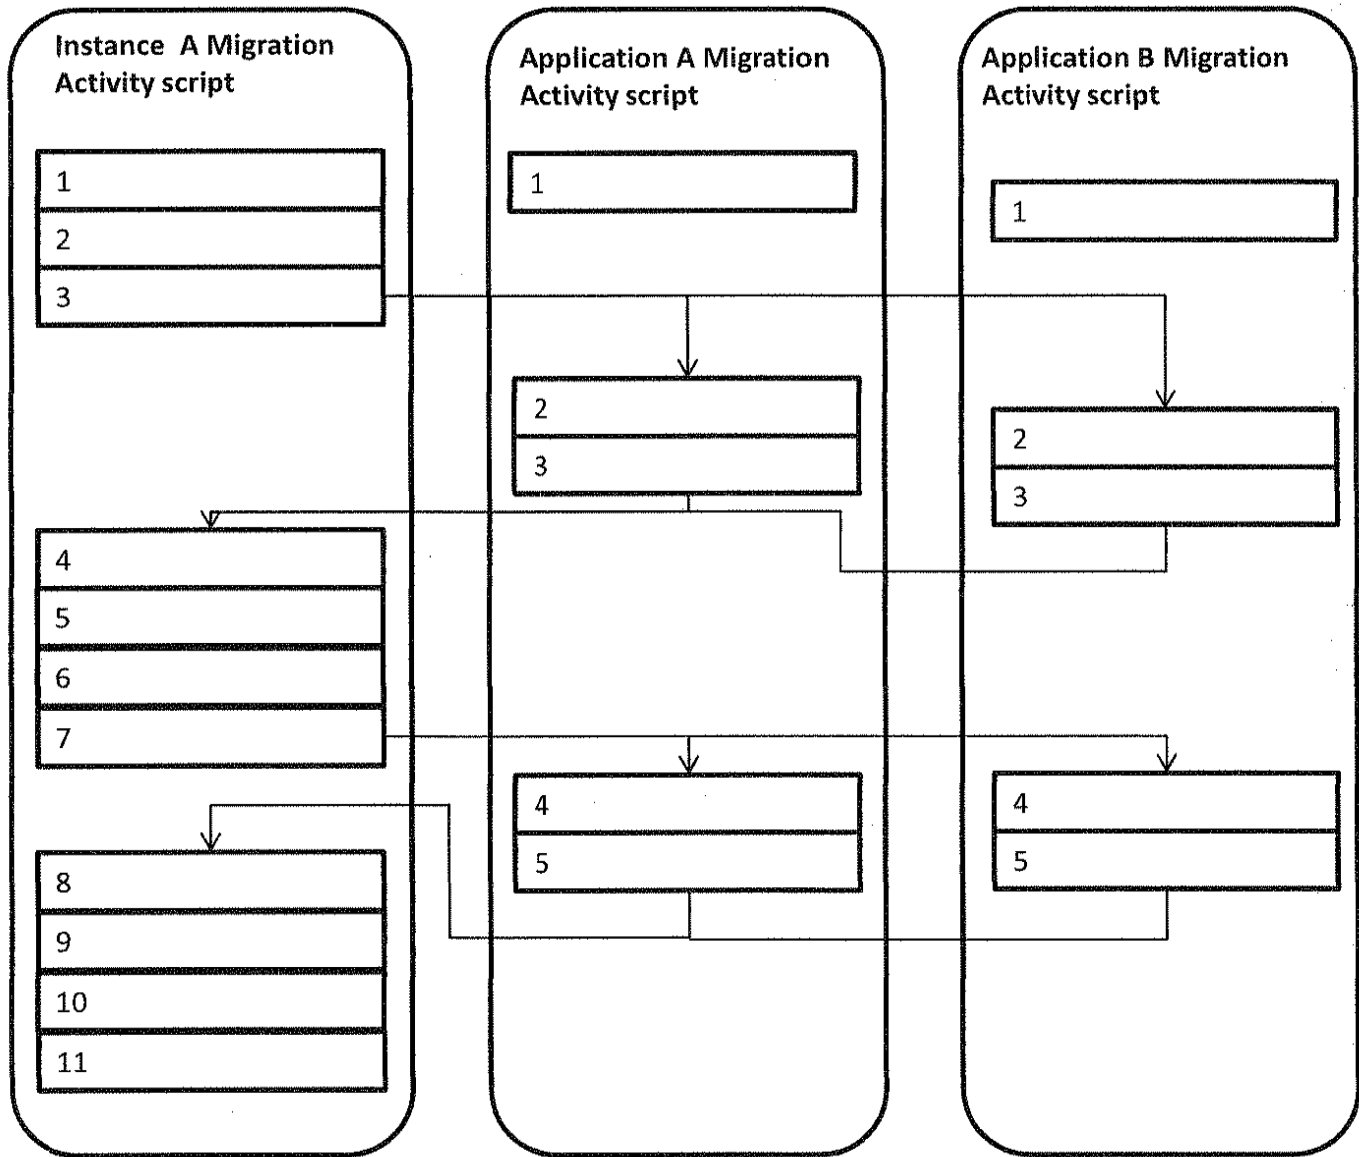
Bundle Unit 61

FIG. 6C

Hour By Hour Bundle Schedule

List of T-Zero & Backout Activities for the Bundle in Chronological Order

Bundle 61

Date	Planned Start	Planned End	Duration (hh:mm)	Team Name	Assigned User	Migration Bundle	Entity Type	Entity Name	Entity Seq #	Activity	Dependencies
T Zero - Scheduled Activities											
12/07/12	16:00	16:15	0:15	ME - Workload Scheduling	Employee A	Bundle 61	Instance	Instance A		1. Place Job Scheduler Job(s) on Hold	
12/08/12	19:45	20:00	0:15	ME - Monitoring	Employee B	Bundle 61	Instance	Instance A		2. Disable Monitoring on	
12/08/12	20:00	20:30	0:30	ME - Windows Admin	Employee C	Bundle 61	Instance	Instance A		3. Server Cut-Over	
12/08/12	20:30	20:45	0:15	ME - Windows Admin	Employee C	Bundle 61	Instance	Instance A		4. Update WINS Entries	
12/08/12	20:45	21:15	0:30	ME - Windows Admin	Employee C	Bundle 61	Instance	Instance A		5. Re-install VMWare tools	
12/08/12	21:15	21:30	0:15	ME - DNS	Employee D	Bundle 61	Instance	Instance A		6. DNS push from old IP to new IP	
12/08/12	21:30	21:45	0:15	ME - Windows Admin	Employee C	Bundle 61	Instance	Instance A		7. Configure client backups	
12/08/12	21:45	22:00	0:15	ME - Windows Admin	Employee C	Bundle 61	Instance	Instance A		8. Apply latest Antivirus policies	Successors: Application A - (1)
12/08/12	22:00	22:30	0:30	App Admin	Employee E	Bundle 61	Application	Application A		1. Post-Startup	Predecessors: Instance A - (8)
12/08/12	23:15	23:30	0:15	ME - Workload Scheduling	Employee F	Bundle 61	Application	Application A		2. Verification-Testing	Successors: Application B - (1)
12/08/12	23:30	23:45	0:15	ME - Wave Team	Employee G	Bundle 61	Application	Application B		1. Bundle Move Forward Decision	Predecessors: Application A - (2) Successors: Instance A - (9)
12/08/12	23:45	00:15	0:30	ME - Monitoring	Employee F	Bundle 61	Instance	Instance A		9. Enable Monitoring on the Server	Predecessors: Application B - (1)
12/09/12	00:15	00:30	0:15	ME - Workload Scheduling	Employee F	Bundle 61	Instance	Instance A		10. Release Job Scheduler Job(s)	
12/09/12	00:30	00:45	0:15	ME - Windows Admin	Employee F	Bundle 61	Instance	Instance A		11. Tag Migration Completed Within CMDB	Successors: Application B - (2)
12/09/12	00:45	01:45	1:00	ME - Wave Team	Employee G	Bundle 61	Application	Application B		2. Operations Accepts Bundle Implementation	Predecessors: Instance A - (11)

FIG. 7

800


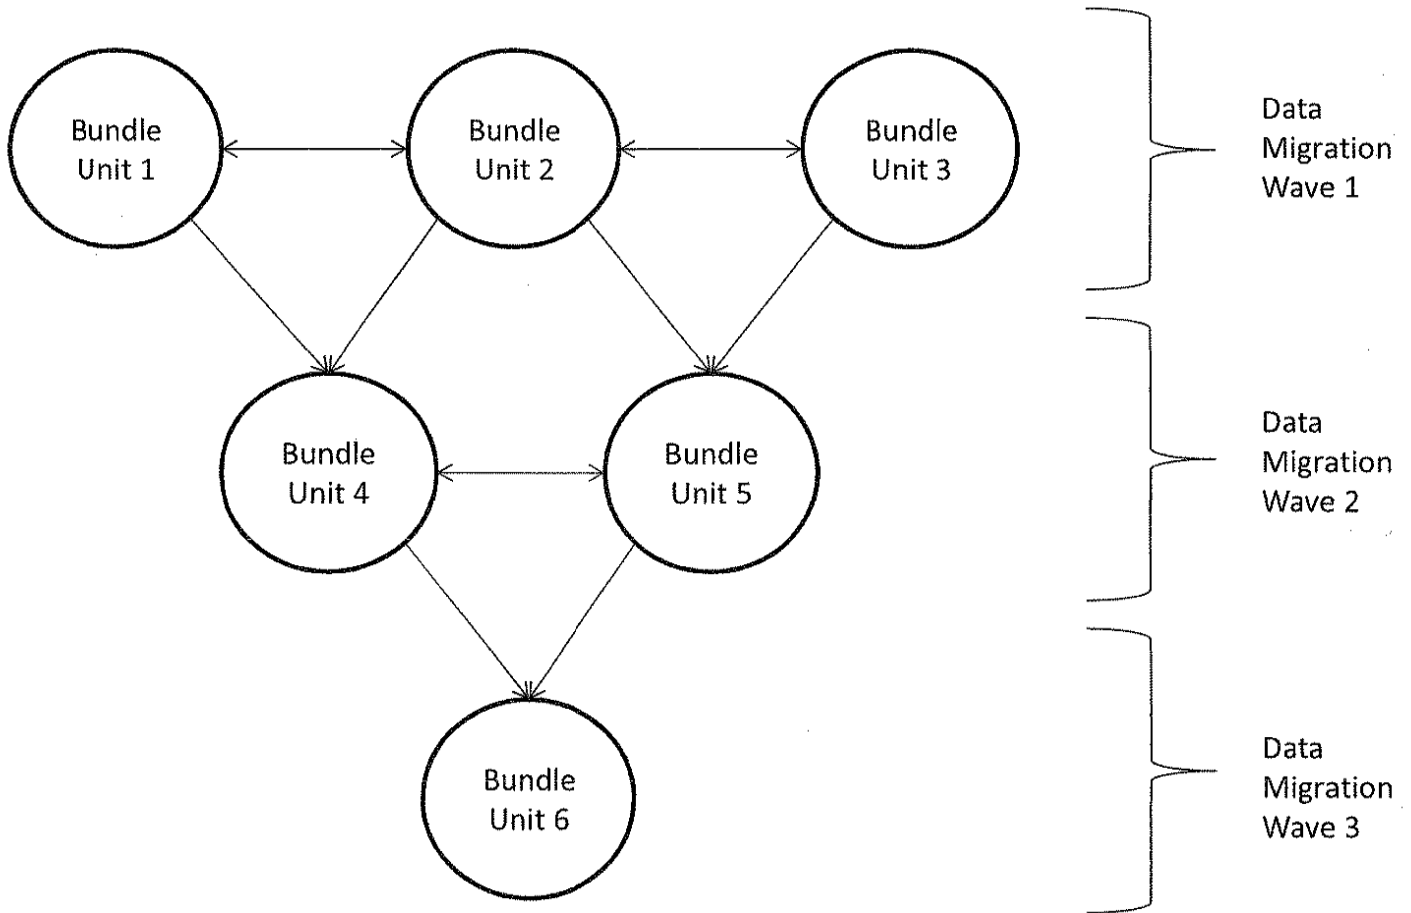


FIG. 8

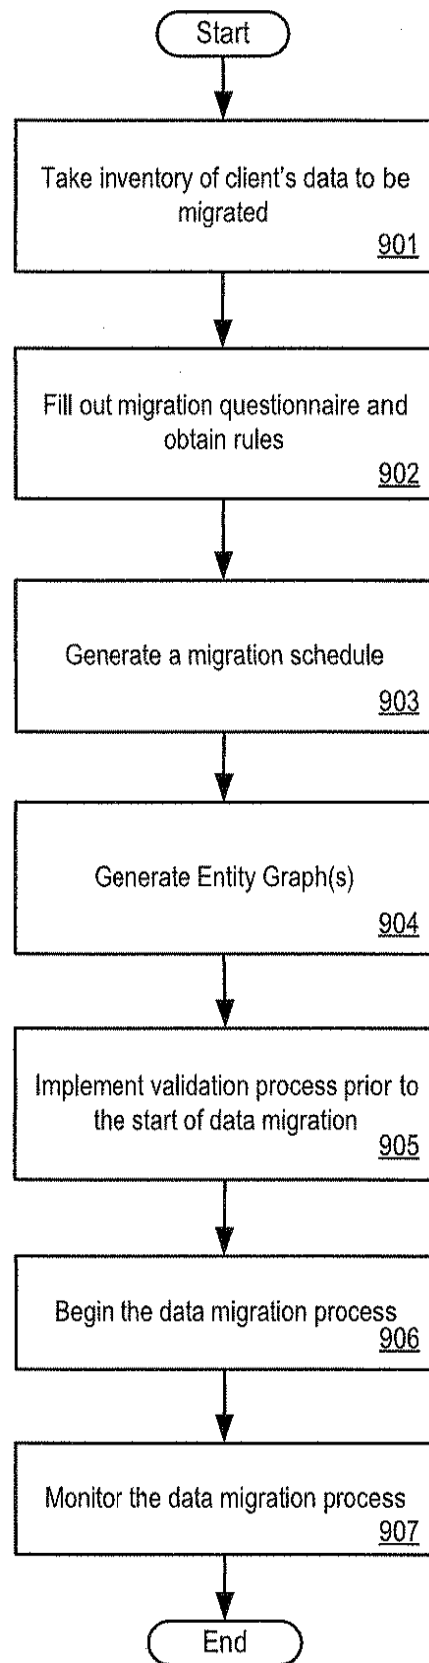

900

FIG. 9A

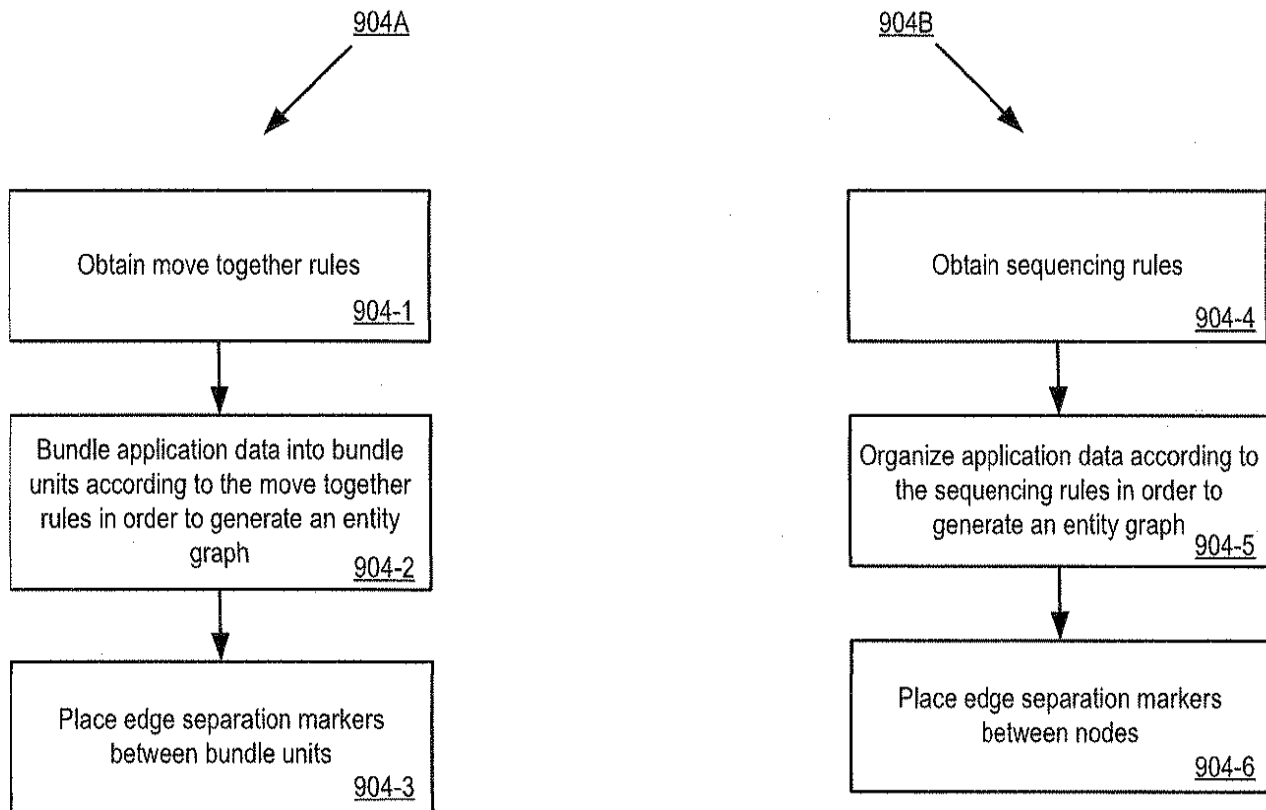


FIG. 9B

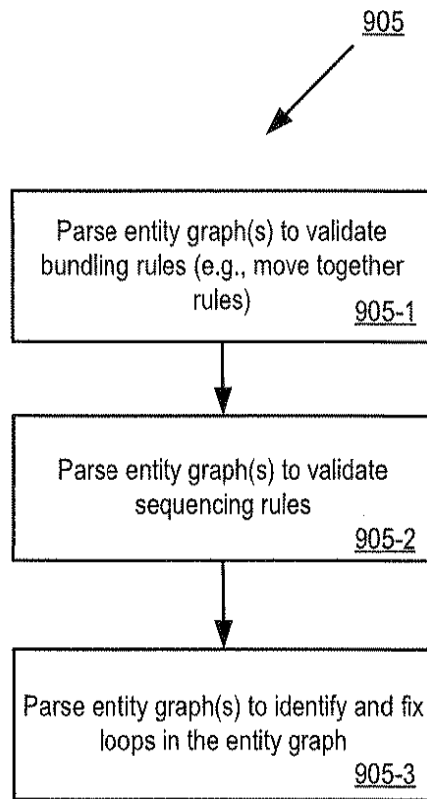


FIG. 9C

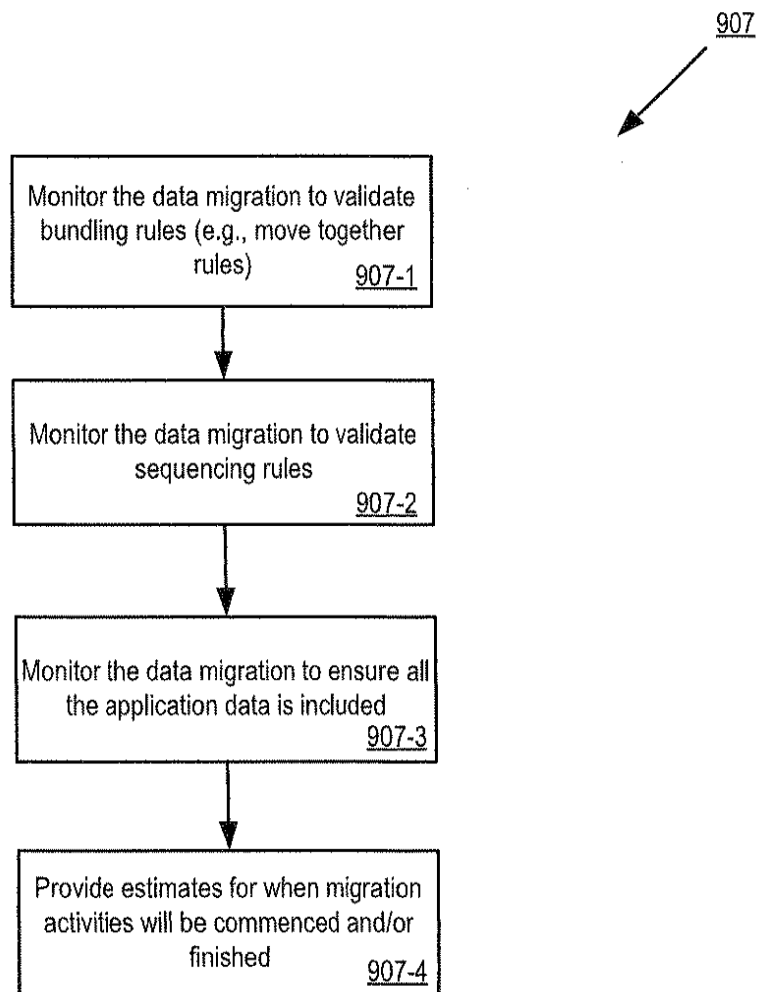


FIG. 9D

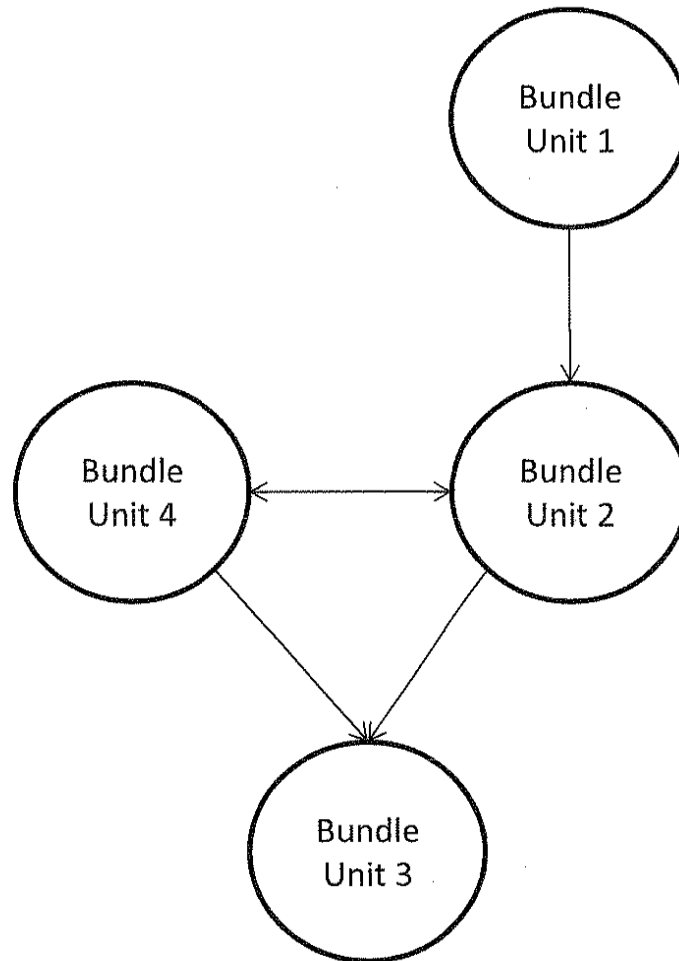
1000

FIG. 10
